



GROUP 2

St. Kitts & Nevis

COUNTRY	WEEK	METHODOLOGIST	SUBMITTED	STATUS
St. Kitts & Nevis	Week 10 · 2026	Leo Cursino Fisiologo, Preparacion Fisica · Basketball	July 16, 2026	Approved

Phase 01 · Apr 27 – Aug 9, 2026

ACTIVITIES COMPLETED



0

of 1 logged this week

STRATEGIC INITIATIVES



1

Tracked this week

STAKEHOLDER
ENGAGEMENTS



2

This week

SUPPORT NEEDS



0

Open items

INITIATIVE PROGRESS & TREND

INITIATIVE

CATEGORY

WEEKLY PROGRESS

STATUS

Physical Education Implementation and Teacher Certification Program

Educational

10%

Delayed

KEY ACTIVITIES THIS WEEK

DATE

ACTIVITY

STATUS

Jul 1 Meeting with SkNOC to define next steps following the failure to meet the deadline provided by the Attorney General's Office.

Pending

STAKEHOLDER ENGAGEMENT OVERVIEW

ENGAGEMENT BY LEVEL

STAKEHOLDERS BY TYPE

Institutional




NOC Leadership

2

2 total engagements this week, across 1 stakeholder type.

WEEKLY PROGRESS TREND (ALL INITIATIVES)

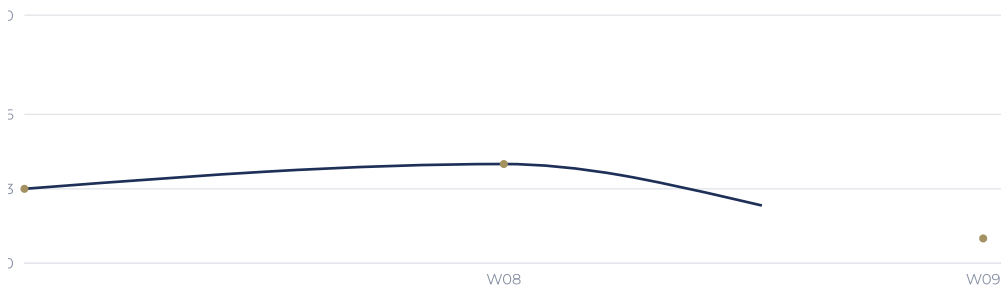

THIS WEEK'S OBJECTIVES

- 1 Wait for the deadline proposed by the government for the 30th and determine the next steps after this cutoff date

Expected result — We hope the deadline is met and that we can move forward.

Success indicator — if we manage to sign the agreement and launch the proposed plan

EXECUTIVE SUMMARY


We have not received a response from the government regarding the proposed activities; we are currently adjusting the plan and considering solutions to the challenges.

INITIATIVE PROGRESS

Physical Education Implementation and Teacher Certification Program

● Delayed

EDUCATIONAL



No change vs. last week

The proposed plan involves the Ministry of Education and Sports and the sports federations; however, without official government endorsement, we lack access to the budget and cannot move forward, as each stakeholder also requires this official authorization.

PANAM SPORTS SUPPORT NEEDED

We are considering seeking a meeting with Panam to clarify the points and consult on the new strategies.

NEXT WEEK FOCUS

Revise the plan for SKN, incorporating new dates and steps to address the identified needs within new timeframes.
